

UTILITY SERVICE  
CUSTOMER SERVICE  
535 COURTNEY HODGES BLVD  
P.O. BOX 1350  
PERRY, GA 31069  
TEL 800-223-3695  
FAX 478-987-2529  
WWW.UTILITYSERVICE.COM




## City Of Winchester Public Utilities Visual Inspection Report

### Tank Information for Customer # 8160

- **Tank Name:** Jefferson Street Tank
- **Tank Size/Style:** 3,800,000 Gst
- **Tank Location:** Jefferson Street
- **Project Number:** 101153
- **Service Request:** 359117
- **Inspection Date:** October 25, 2012
- **Report Author:** B\_ETHERIDGE
- **Inspected By:** Larry Palmer

### Customer Contact Information

- **Administrative:** Perry Eisenach
- **Job:** Mitch Thomas
- **Address:** 15 North Cameron Street  
P O Box 75  
Winchester, VA 22601
  
- **Telephone:** 540-667-1815

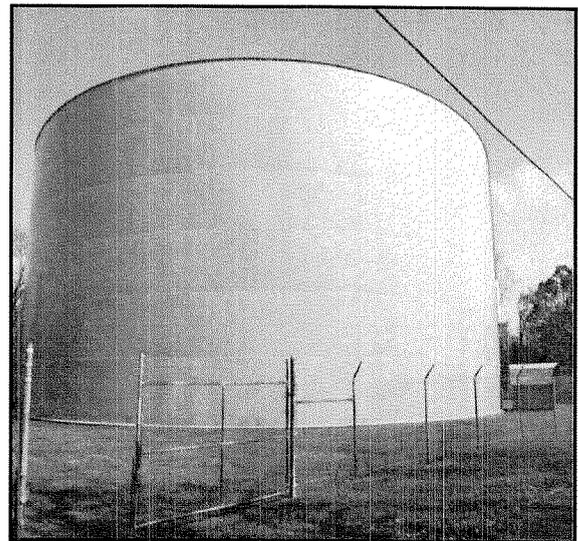

## Summary


A visual inspection was performed on the exterior condition. The tank is in good condition. The interior coating was not fully inspected but will be in 2013 when the interior will be cleaned, inspected and disinfected.

## Coating Type & Conditions

- Interior Coating Condition: The interior coatings were not fully inspected but will be at the next interior inspection, cleaning and disinfection.
- Exterior Coating Condition: Exterior coating is in good condition.

## Safety & Sanitation

- Safety Climbing Devices: Ladders are equipped with secured safety climb devices.
- Access Hatch1: Good
- Vent Screen: Vent screen is in good condition.
- Evidence Of Foreign Matter: No evidence of foreign matter.
- Sediments: Sediment is present in bottom of tank. Tank will be cleaned at next scheduled washout.

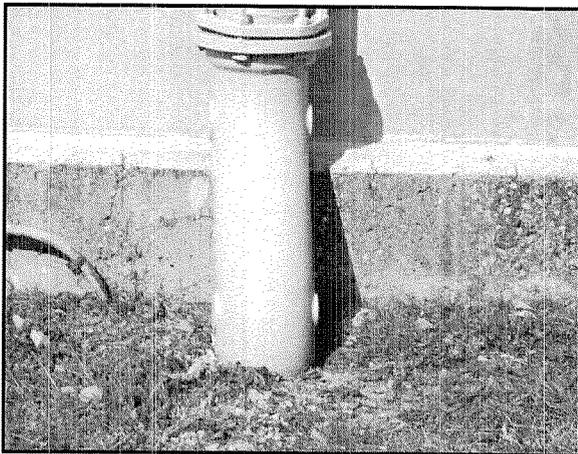


Overflow goes into ground.


## Security

- Fence Around Site: Tank is located inside a fenced-in area.
- Ladder Gate/Access Door: Exterior ladder has a ladder gate installed and is locked.

- Access Hatch Locked: Access Hatch is Secured.
- Evidence Of Vandalism: There is not evidence of vandalism.

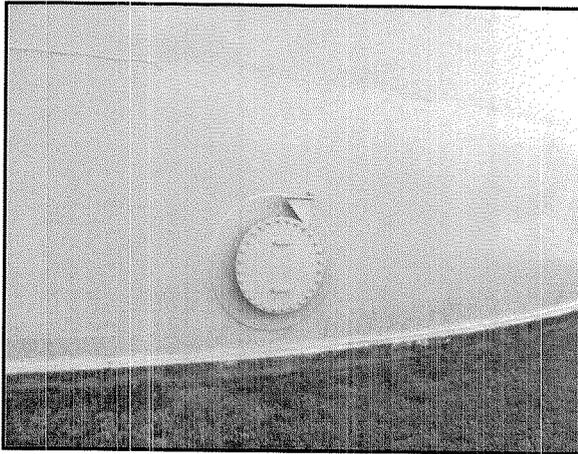

Shell manway is secure.

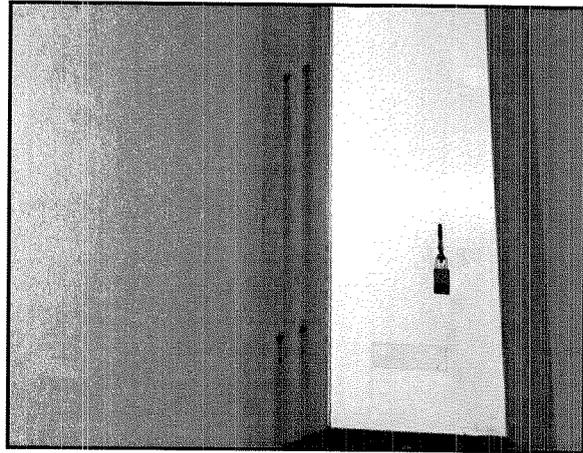

Ladder gate is secured.

### **Structural**

- Foundation: Foundation is in good condition and there is no erosion occurring around foundation.
- Access Ladders: Dry-side access ladder styles, rungs and connections are in good condition.
- Watertight Conditions: There are no visible leaks at the time of the inspection.
- Interior Ladders: Interior ladder stiles, rungs and connections are in good condition.
- Roof: Roof Trusses, Rafters and their connections are sound and in good condition.
- Vents: Vent is in Good Condition.
- Overflow Pipe: Overflow Pipe is in good condition.
- Welds: Weld Seams are in good condition.
- Float System: Float system is in good working condition.
- Level Indicator: Level indicator is in good working condition.
